



A Modified AGILE Approach to Project Management

October 14, 2015



Knowledge. Performance. Impact.

Introduction



Sheri D. Weppel
Director of eLearning and
Training Development




On Twitter? 

Expand the conversation by following [@GPCorp](#) using the hashtag [#AGILE](#)

What Are the Stops on This **WEBINAR**?



Social Contracting

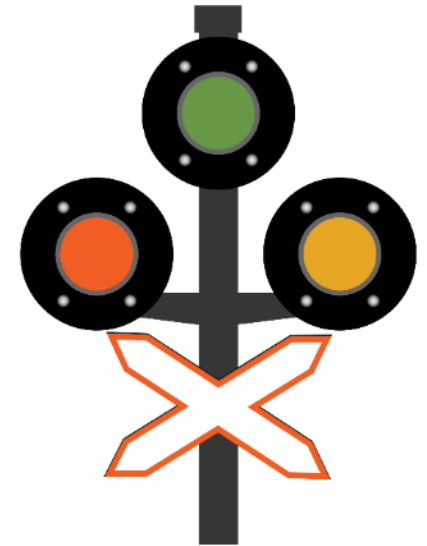

Stage Gate Process



Team-Based Portals


What are the areas that quickly **impact** your scope?




Waterfall Versus **AGILE**

Design PROCESS

WATERFALL ADDIE PROCESS

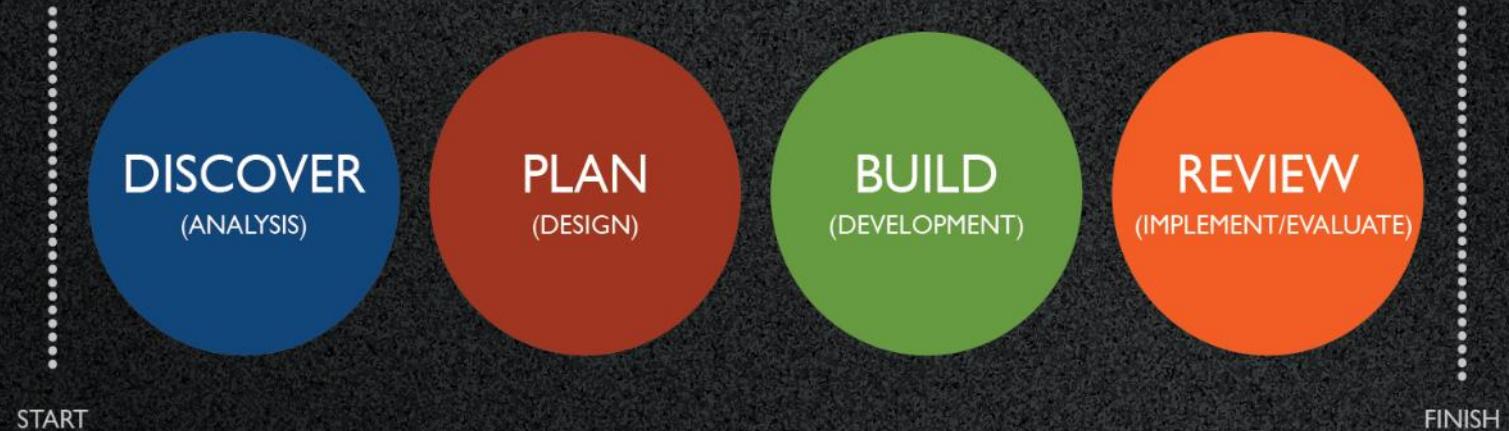


AGILE APPROACH

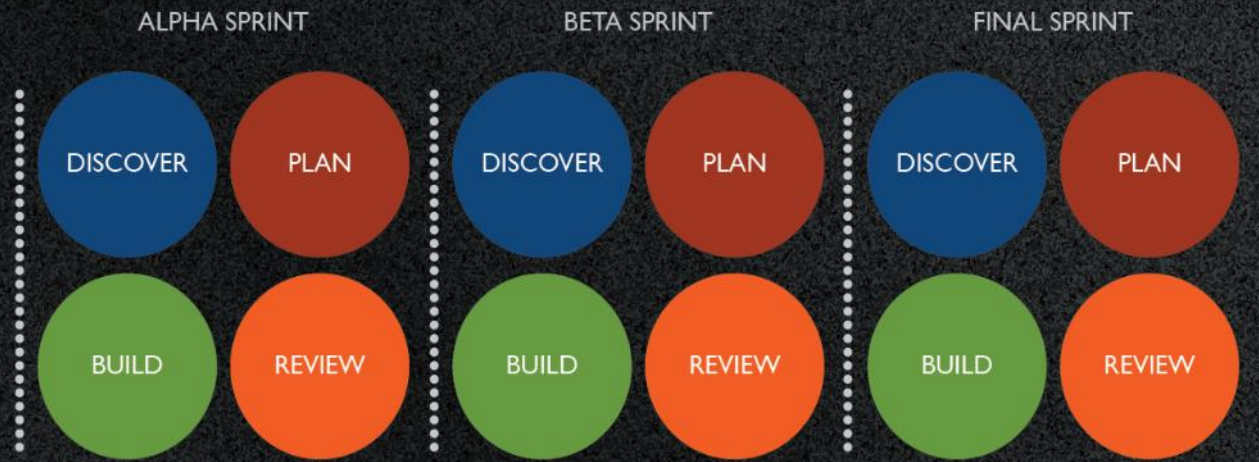




Social CONTRACTING


Finalization of the DELIVERABLES

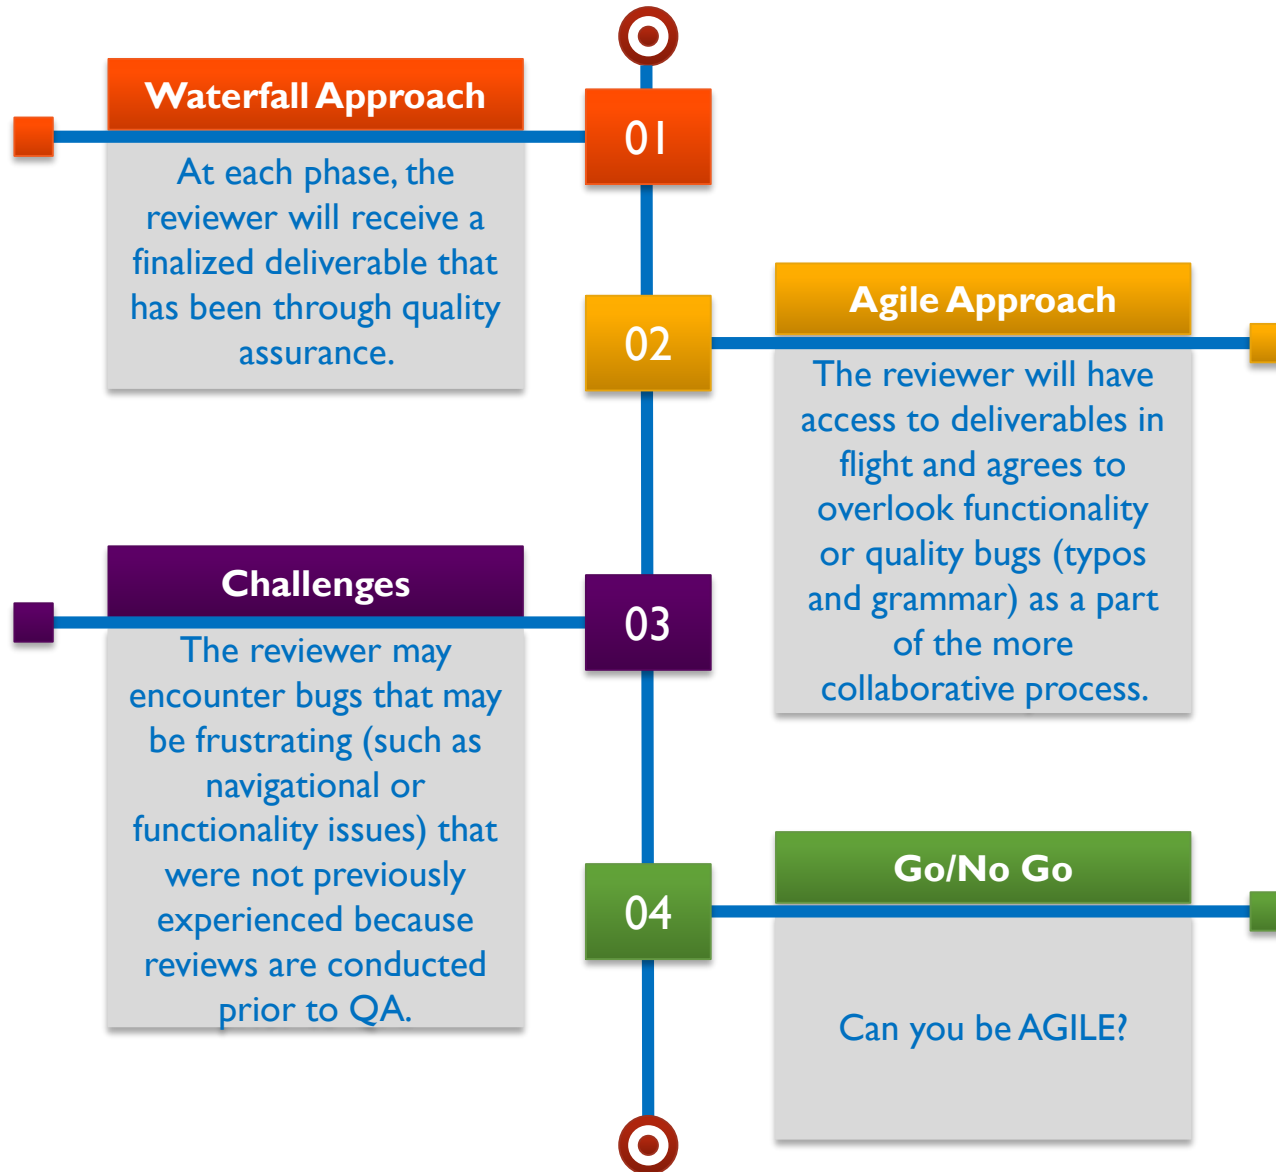


Amount of CHANGES

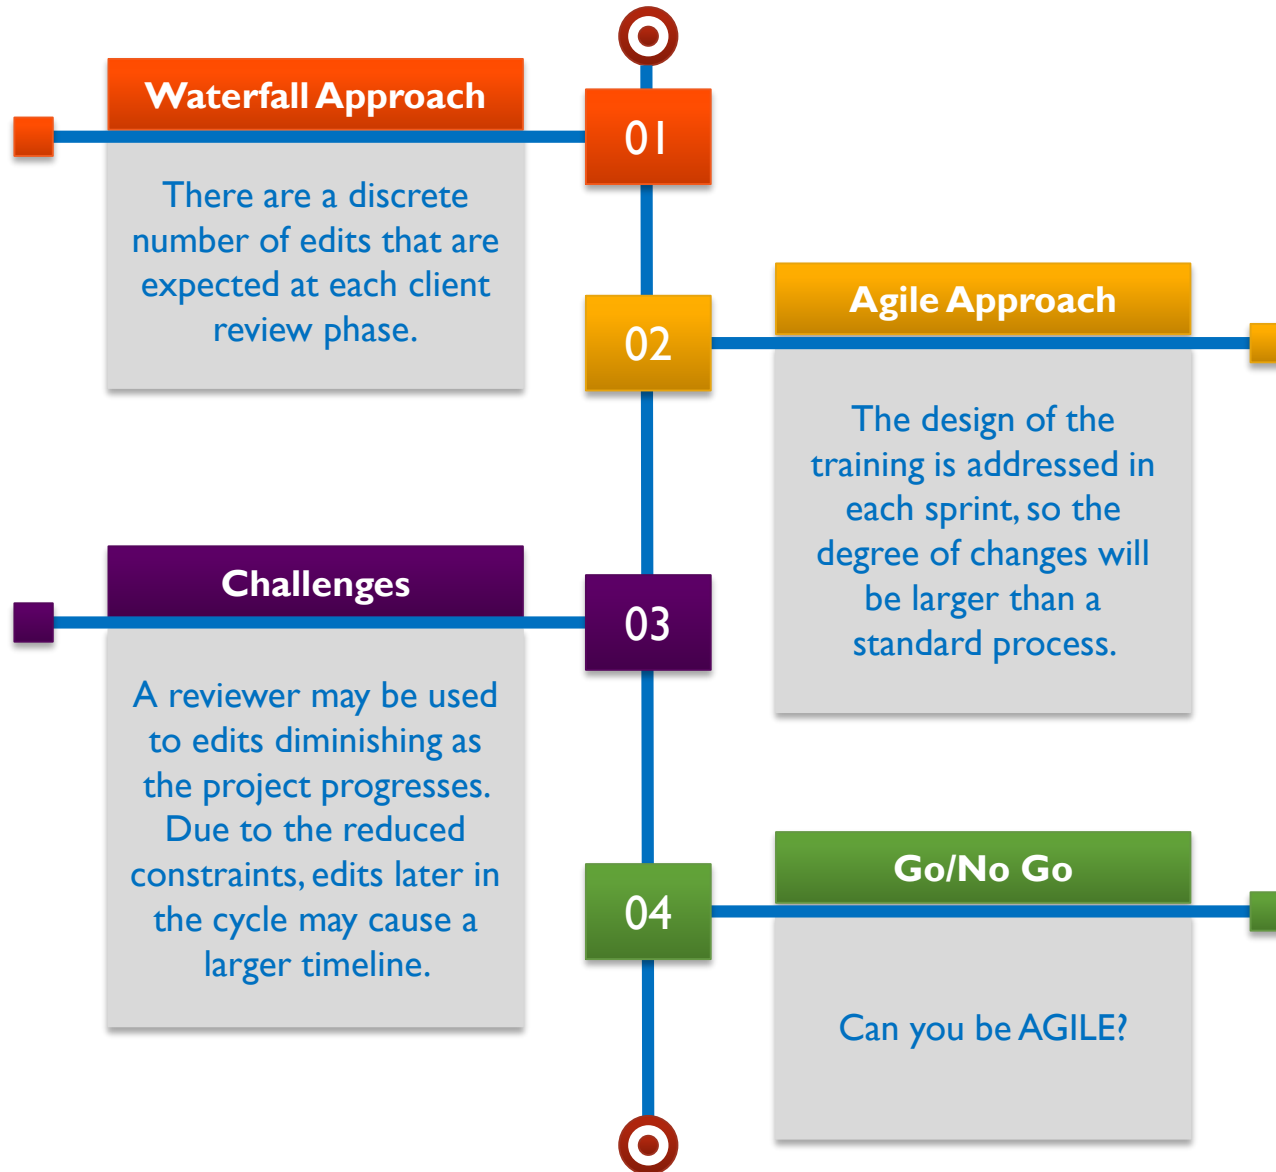

Review CYCLES

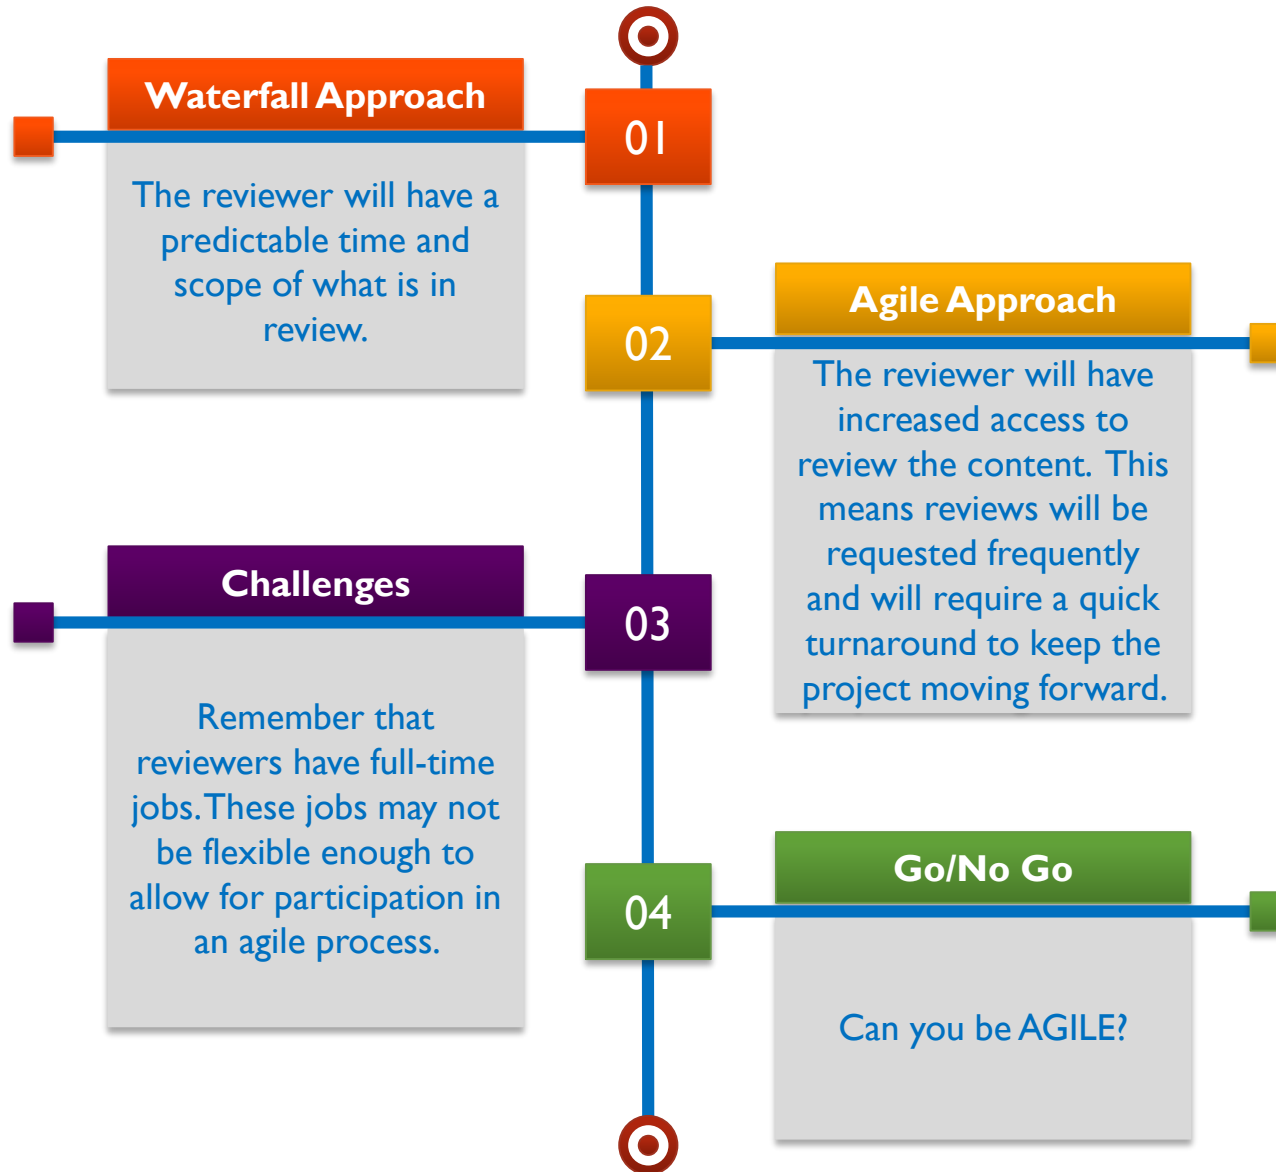


SCRUM Meetings

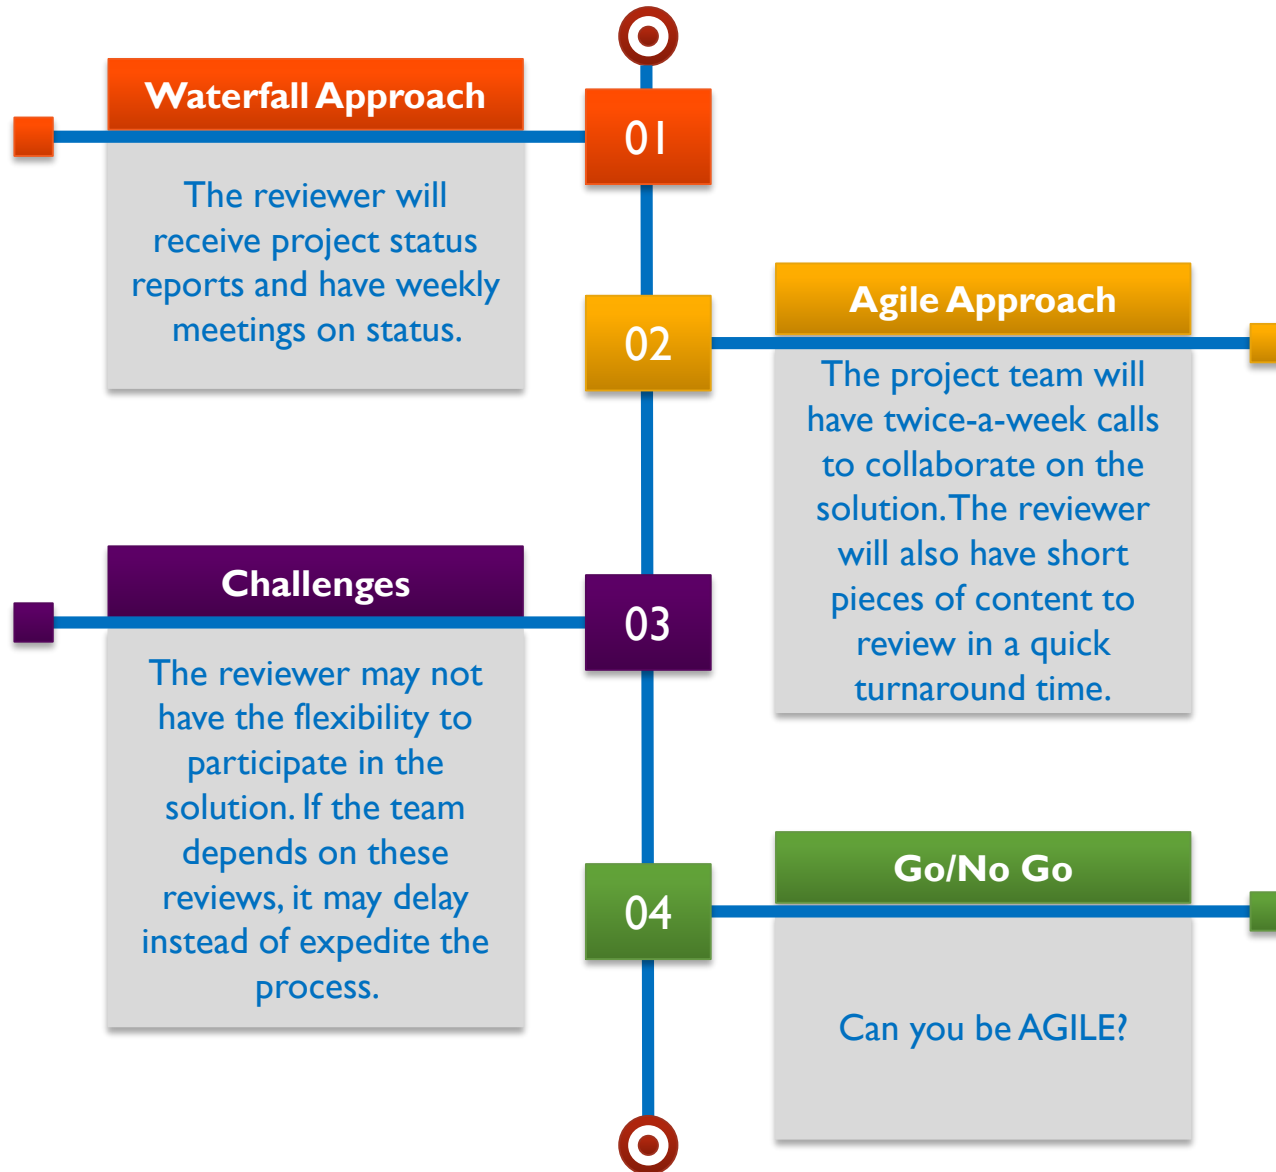

Development TOOLS



Product BACKLOG

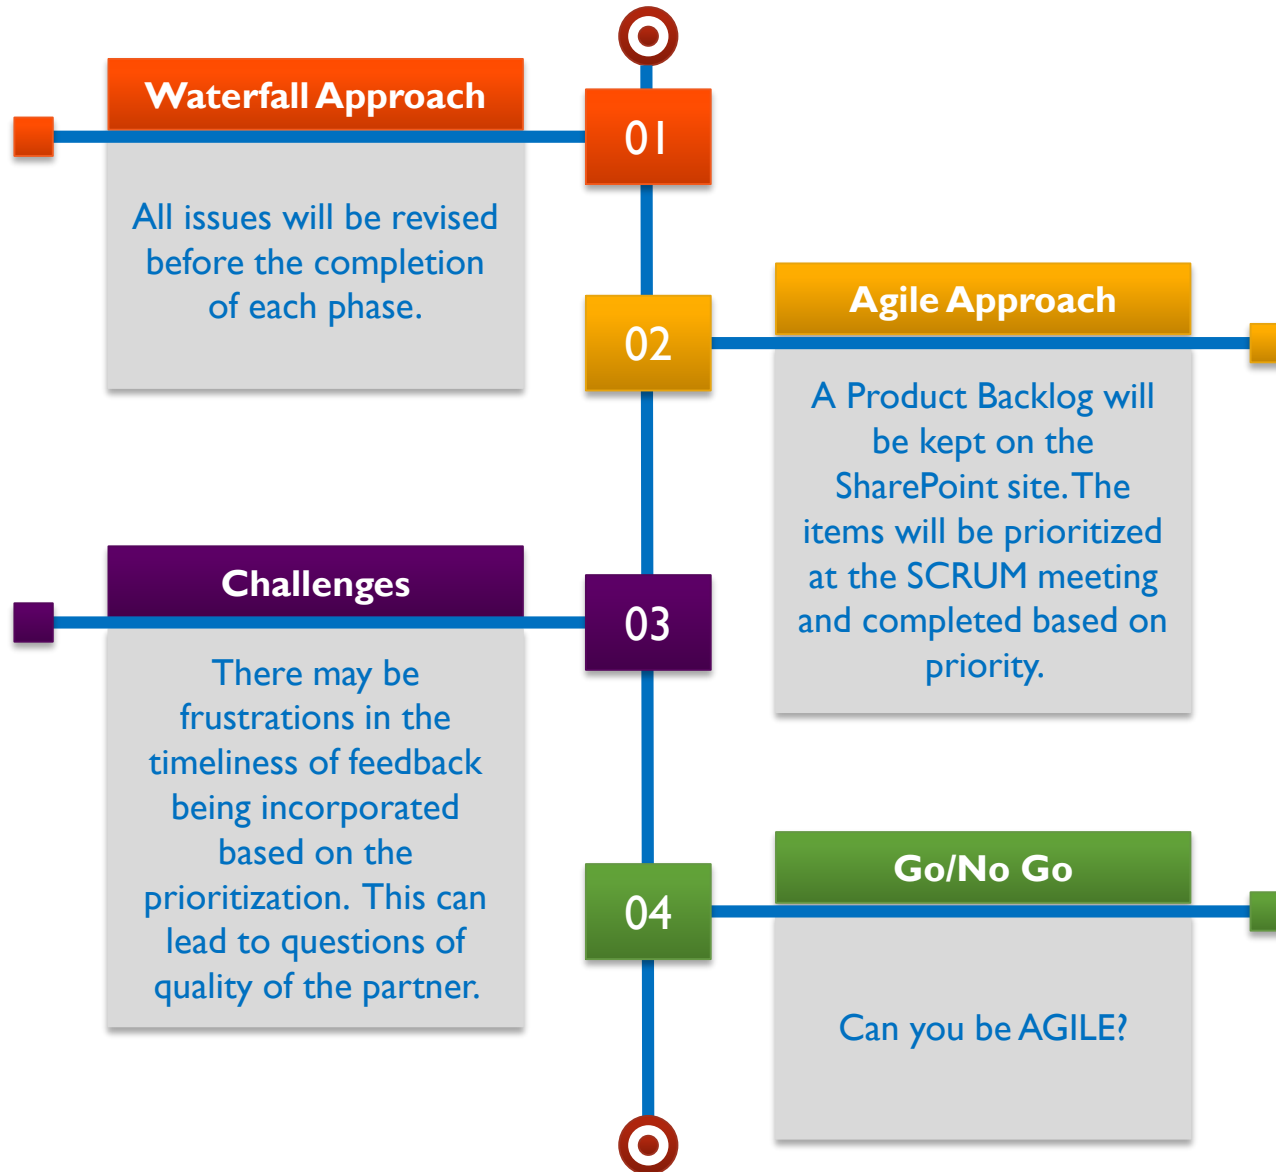



Team-Based PORTALS

What are your biggest
challenges keeping projects
on a timeline?

A Common Place to MEET



Team-Based PORTAL

- Surveys
- Design Checklist
- Pictures
- Documents
- ForQA
- QAedDocuments
- 01_HowtoLogintoBLIS
- 02_Navigation
- 03_Search
- 04_ViewPrintSave

Project Schedule

<input type="checkbox"/>	@	Module	Storyboard	SB Feedback	Alpha	Alpha Feedback	Beta	Beta Feedback	Gold	Gold Feedback
		Mod 1	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
		Mod 2	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
		Mod 3	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
		Mod 4	Approved	Received	Approved	Received	Approved	Received	Approved	Approved

Gold Links for Testing

<input type="checkbox"/>	Title	Content Server Link	Completion	Status
	Module 01	https://lmscontent.client.com/Mod1/LMS-launch.html	PASSED	Tested
	Module 02: GA	https://lmscontent.client.com/Mod2_GA/LMS-launch.html	PASSED	Tested
	Module 02: CL	https://lmscontent.client.com/Mod2_CL/LMS-launch.html	PASSED	Tested
	Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested
	Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested
	Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested

Timeline Shifts

Timeline Adjustments

by Weppel, Sheri

3/16/2011 2:42 PM

All timelines have been reset to TBD awaiting feedback. New timelines will be added when feedback is received. The approximate wait time for re-release is:

Beta Modules: 5 business days
 Gold Modules: 3 business days
 Gold Edits: 2 business days

Estimated Course Duration

<input type="checkbox"/>	@	Number	Topic Title	Slide Count	Slide Total
		1	How to Login	18	18
		2	Navigation	25	43
		3	Search	44	87
		4	View, Print, Save	25	112

Approved to Move to the Next Develop...

Type Name Modified By
 Completed Weppel, Sheri
 (More Documents...)

Add document

Feedback Requiring Repeat Project Cycle

Type Name
 Completed
 Add document

Beta Modules for Review

Beta Module 10

Add new link

Project Schedule

Final Testing Links

Timeline Shifts

Scope Overview

Approval Process

To Do List

Team-Based PORTAL

- Surveys
- Design Checklist
- Pictures
- Documents
- ForQA
- QAedDocuments
- 01_HowtoLogintoBLIS
- 02_Navigation
- 03_Search
- 04_ViewPrintSave

Project Schedule

<input type="checkbox"/>	Module	Storyboard	SB Feedback	Alpha	Alpha Feedback	Beta	Beta Feedback	Gold	Gold Feedback
<input type="checkbox"/>	Mod 1	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 2	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 3	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 4	Approved	Received	Approved	Received	Approved	Received	Approved	Approved

Gold Links for Testing

<input type="checkbox"/>	Title	Content Server Link	Completion	Status
<input type="checkbox"/>	Module 01	https://lmscontent.client.com/Mod1/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 02: GA	https://lmscontent.client.com/Mod2_GA/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 02: CL	https://lmscontent.client.com/Mod2_CL/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested

Approved to Move to the Next Develop...

Type	Name	Modified By
	Completed	Weppel, Sheri

(More Documents...)

[+ Add document](#)

Feedback Requiring Repeat Project Cycle

Type	Name
	Completed

[+ Add document](#)

Beta Modules for Review

Beta Module 10

Collaborate on the project schedule to give each other and stakeholders a minute-by-minute status report.

3 Search
4 View, Print, Save

44 87
25 112

Team-Based PORTAL

- Surveys
- Design Checklist
- Pictures
- Documents
- ForQA
- QAedDocuments
- 01_HowtoLogintoBLIS
- 02_Navigation
- 03_Search
- 04_ViewPrintSave

Project Schedule

<input type="checkbox"/>	Module	Storyboard	SB Feedback	Alpha	Alpha Feedback	Beta	Beta Feedback	Gold	Gold Feedback
	Mod 1	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
	Mod 2	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
	Mod 3	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
	Mod 4	Approved	Received	Approved	Received	Approved	Received	Approved	Approved

Gold Links for Testing

<input type="checkbox"/>	Title	Content Server Link	Completion	Status
	Module 01	https://lmscontent.client.com/Mod1/LMS-launch.html	PASSED	Tested
	Module 02: GA	https://lmscontent.client.com/Mod2_GA/LMS-launch.html	PASSED	Tested
	Module 02: CL	https://lmscontent.client.com/Mod2_CL/LMS-launch.html	PASSED	Tested
	Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested
	Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested
	Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested

Approved to Move to the Next Develop...

Type	Name	Modified By
	Completed	Weppel, Sheri

(More Documents...)

[+ Add document](#)

Feedback Requiring Repeat Project Cycle

Type	Name
	Completed

[+ Add document](#)

Beta Modules for Review

Beta Module 10

Post final files in one location for storage, clarity and reference.

3	Search	44	87
4	View, Print, Save	25	112

Team-Based PORTAL

When changes have the potential to impact the overall timeline, post for clarity and awareness (set alerts for notifications).

Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested
Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested
Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested

Timeline Shifts

Timeline Adjustments

by Weppel, Sheri

3/16/2011 2:42 PM

All timelines have been reset to TBD awaiting feedback. New timelines will be added when feedback is received. The approximate wait time for re-release is:

Beta Modules: 5 business days
Gold Modules: 3 business days
Gold Edits: 2 business days

Estimated Course Duration

<input type="checkbox"/>	@	Number	Topic Title	Slide Count	Slide Total
		1	How to Login	18	18
		2	Navigation	25	43
		3	Search	44	87
		4	View, Print, Save	25	112

Team-Based PORTAL

Project Schedule											Approved to Move to the Next Develop...	
Module	Storyboard	SB Feedback	Alpha	Alpha Feedback	Beta	Beta Feedback	Gold	Gold Feedback	Type	Name	Modified By	
Mod 1	Approved	Received	Approved	Received	Approved	Received	Approved	Approved	Completed		Weppel, Sheri	
Mod 2	Approved	Received	Approved	Received	Approved	Received	Approved	Approved	(More Documents...)			

Keep track of slide counts to ensure all parties remain in scope.

Timeline Shifts

Timeline Adjustments

by Weppel, Sheri

3/16/2011 2:42 PM

All timelines have been reset to TBD awaiting feedback. New timelines will be added when feedback is received. The approximate wait time for re-release is:

Beta Modules: 5 business days

Gold Modules: 3 business days

Gold Edits: 2 business days

Number	Topic Title	Slide Count	Slide Total
1	How to Login	18	18
2	Navigation	25	43
3	Search	44	87
4	View, Print, Save	25	112

Team-Based PORTAL

- Surveys
- Design Checklist
- Pictures
- Documents
- ForQA
- QAedDocuments
- 01_HowtoLogintoBLIS
- 02_Navigation
- 03_Search
- 04_ViewPrintSave

Project Schedule

<input type="checkbox"/>	Module	Storyboard	SB Feedback	Alpha	Alpha Feedback	Beta	Beta Feedback	Gold	Gold Feedback
<input type="checkbox"/>	Mod 1	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 2	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 3	Approved	Received	Approved	Received	Approved	Received	Approved	Approved
<input type="checkbox"/>	Mod 4	Approved	Received	Approved	Received	Approved	Received	Approved	Approved

Gold Links for Testing

<input type="checkbox"/>	Title	Content Server Link	Completion	Status
<input type="checkbox"/>	Module 01	https://lmscontent.client.com/Mod1/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 02: GA	https://lmscontent.client.com/Mod2_GA/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 02: CL	https://lmscontent.client.com/Mod2_CL/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested
<input type="checkbox"/>	Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested

Approved to Move to the Next Develop...

Type	Name	Modified By
	Completed	Weppel, Sheri

(More Documents...)

[+ Add document](#)

Feedback Requiring Repeat Project Cycle

Type	Name
	Completed

[+ Add document](#)

Beta Modules for Review

Beta Module 10

Use document libraries as a form of approval process (approved and repeat cycle).

3	Search	44	87
4	View, Print, Save	25	112

Team-Based PORTAL

Project Schedule

Approved to Move to the Next Develop...

Include a To Do list for reviewers to post items in need of review.

Module 02: CL	https://lmscontent.client.com/Mod2_CL/LMS-launch.html	PASSED	Tested	+ Add document
Module 03	https://lmscontent.client.com/Mod3/LMS-launch.html	PASSED	Tested	
Module 04: GA	https://lmscontent.client.com/Mod4_GA/LMS-launch.html	PASSED	Tested	
Module 04: CL	https://lmscontent.client.com/Mod4_CL/LMS-launch.html	PASSED	Tested	

Timeline Shifts

Timeline Adjustments

by Weppel, Sheri

3/16/2011 2:42 PM

All timelines have been reset to TBD awaiting feedback. New timelines will be added when feedback is received. The approximate wait time for re-release is:

Beta Modules: 5 business days

Gold Modules: 3 business days

Gold Edits: 2 business days

Estimated Course Duration

<input type="checkbox"/>	@	Number	Topic Title	Slide Count	Slide Total
		1	How to Login	18	18
		2	Navigation	25	43
		3	Search	44	87
		4	View, Print, Save	25	112

Beta Modules for Review

Beta Module 10

[+ Add new link](#)



Stage Gate **PROCESS**

CHECKPOINTS

There are a few checkpoints to include in your project:



Stage gates are set to ensure certain elements are finalized before project costs (such as narration and purchasing of stock photos/videos) are expended.



There are still stakeholder reviews to consider. Determining the proper stage gate will ensure the product is in a “steady state” for that level of reviewer.




Projects still have deadlines and go-live dates. Checkpoints ensure projects do not enter a do-loop of edits without ever progressing to completion.




Key TAKEAWAYS

REMINDERS

WATERFALL ADDIE PROCESS

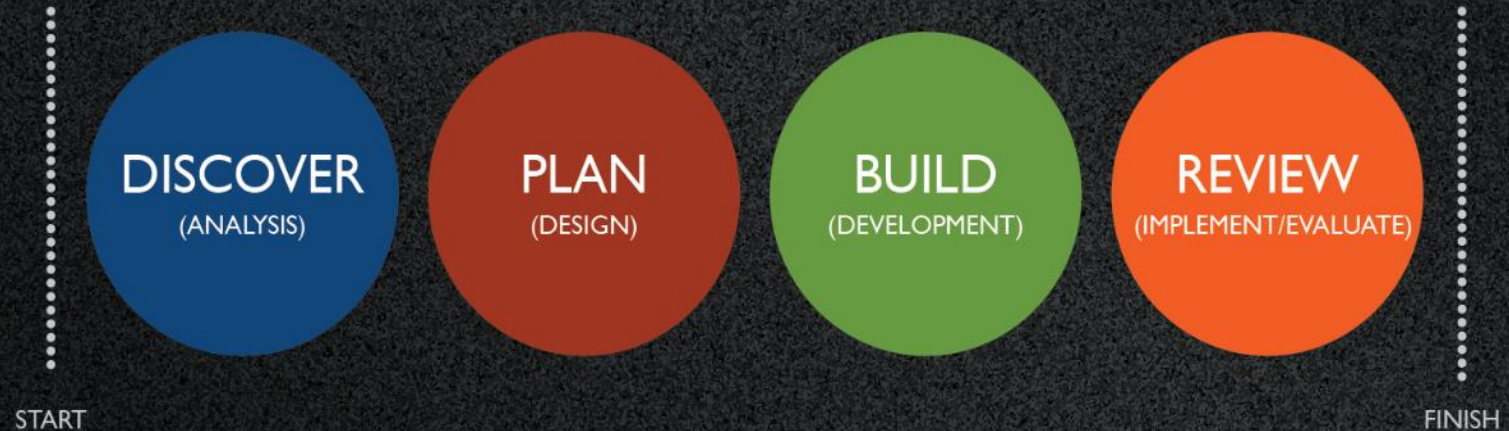


MODIFIED AGILE APPROACH

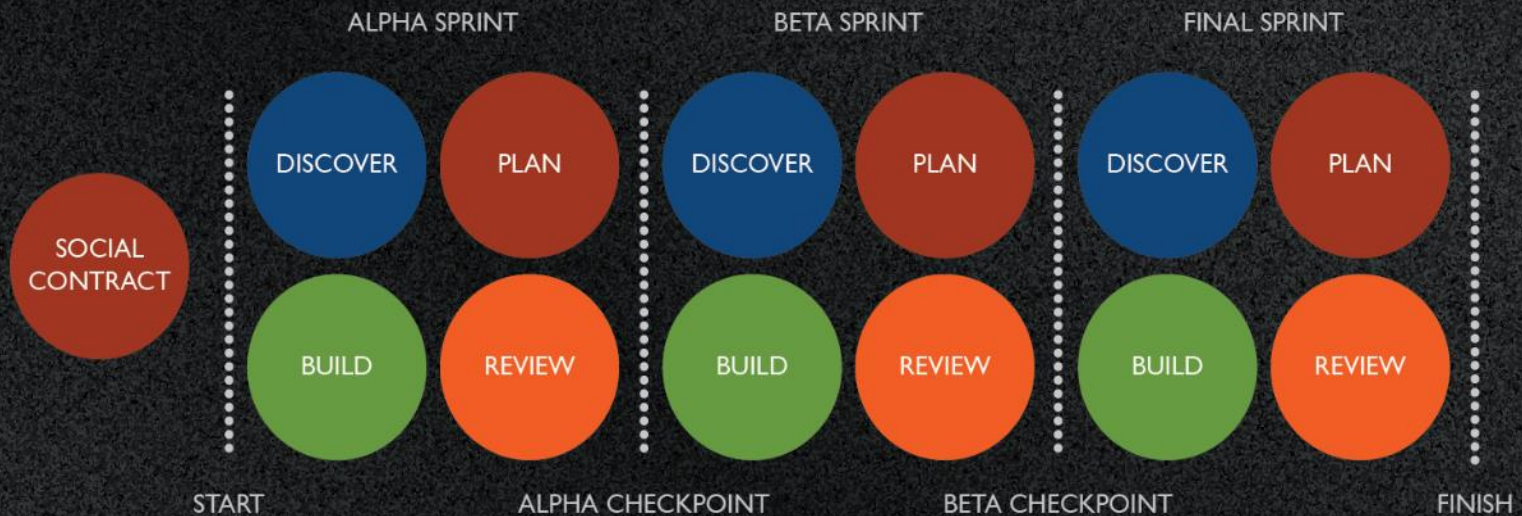

Key TAKEAWAYS



Social Contracting

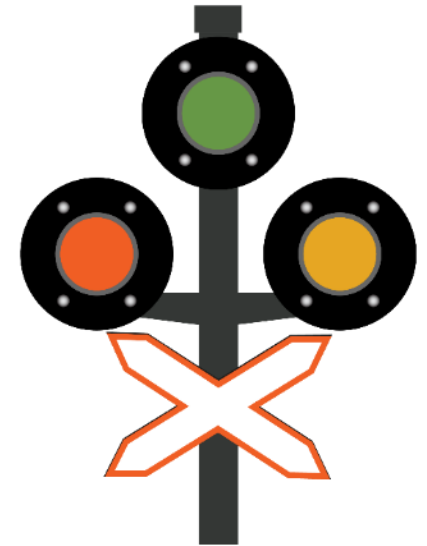

Stage Gate Process



Team-Based Portals

gpstrategies.com

Sheri Weppel

Director of eLearning
and Training Development

sweppel@gpstrategies.com

Phone 484.949.1354

Twitter: @Weppels

